

Information to the board and members of Rotary Korsoer/Denmark about the Tushikane e.V. project boyshostel in Mapanda/Tansania

What's new:

Construction phases 1 and 2, i.e. the foundation and the shell without the roof, were completed on schedule at the end of September 2021.



Picture: Shell of the Men's hostel end of Sept.

Some numbers:

Transferred first installment according to cost estimate for phase construction 1+2:

63 000 000 TZS (approx. 24 000 Euro).

Actual costs according to receipts:

63 181 000 TZS (= 24 300 €).

We have received a complete cost statement from Thobias Pugili. The planning and compilation of the cost vouchers is very exemplary! Great praise to Thobias!

At the end of September the second installment for the boys hostel was transferred without any transition:

27 000 € = 71 040 000 TZS.

From the end of September to mid-November, most of the roof truss was installed. The work stagnated a bit, because the construction manager Baba Injinia had to travel to his home in the north of Tanzania for 3 weeks due to a private matter. Since mid-November the work has started again. The material for the roof is already available. According to Thobias Pugili, the plan is still to complete the building by the end of December 2021.



Picture: Shell + work on the roof truss for the boy's hostel.

The planning for the water supply has not been done yet, this is still pending. A combination of a well and rainwater harvesting from the roof with a cistern is to be created. For this the Tushikane project team Men's hostel estimated costs in the amount of 15 000 €. Of this amount, Cents for Help Bosch has already pledged €7,000, which is to be transferred at the beginning of 2022.

Scheduled visit to Mapanda:

Furthermore, it is planned that a small delegation from Germany will travel to Mapanda in August 2022 (Sandra, Jürgen, Elisa and Markus). The official handover of Tushikane to the school board and the inauguration of the building will then take place.



Picture: the boy's hostel in the shell state



Image: Construction work at the boy's hostel


Foundation walls
for the boys
hostel



Production of the
stones for the shell

The boys hostel
is growing and
growing....



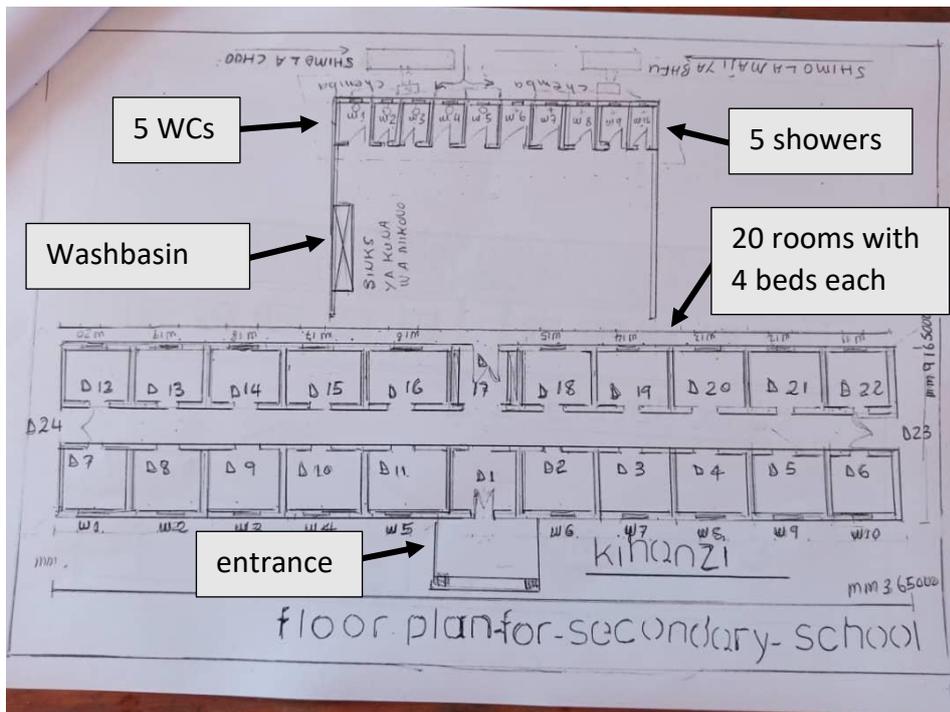

picture: Plan first floor of boy's hostel by Baba Injinia

Cost/Donation Situation:

Planned costs according to Baba Injinia's cost summary are unchanged:

154,076. 500 TZS (= approx. 60,000 EUR). This does not include the water supply.

The promised financial contribution of the district government of TZS 20,000,000 (approx. 7,700 EURO) was promised in October. It is planned that with this contribution a part of the material costs will be paid, e.g. the roof. However, the contribution has not yet reached the project.

Donation list:

2020:	
Lions Club Miltenberg	15 000 €
Cents for Help Bosch	8 000 €
Rotary Denmark	10 000 €
Donations private	12 560€
Total 2020:	45 560€
2021:	
Rotary Denmark	5 375 €
Cents for Help Bosch	5 000 €
Donations private	5 375 €
Total donation:	61 310 €
Pledged donation District Government Mafinga (contribution not yet received)	ca. 7 700 €
Committed donation Cents for Help Bosch for water supply	7 000 €
Grant Tushikane from general donations if needed	20 000 €





15.12.2021

This report was written by Jürgen Gerhart and Sabine Speth, 30.12.2021
